


# Del-Co Flow Test Report



6658 Olentangy River Rd  
Delaware, OH 43015  
(740) 548-7746 Office  
(740) 549-1149 Fax

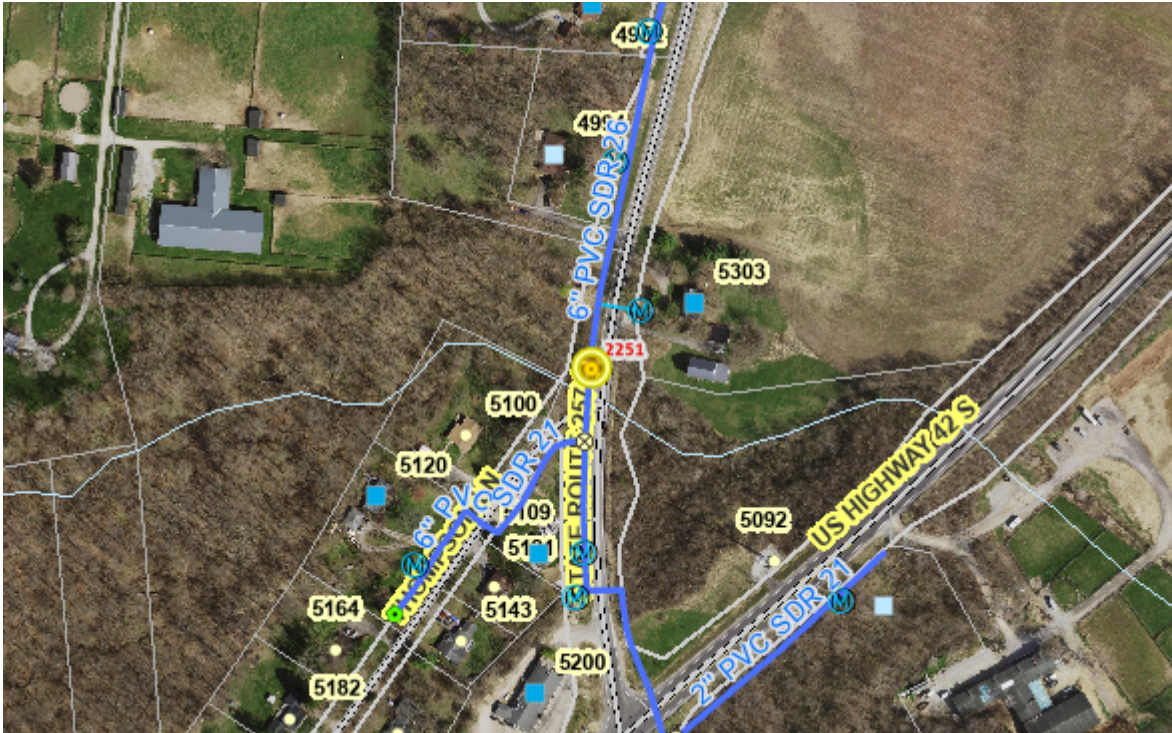

**Date of Test:** 7/3/2024

**Time of Test:** 2:24 PM

**Tester 1:** Chris Hoffman

**Tester 2:** Gregg Frentsos

**Residual Hydrant:** 6781

**Residual Hyd Elev:** 862'

**Test Hydrant:** 2251

**Test Hyd Elev:** 896'

**Approx Dist  
Between Hydrants:** 1,244'

**Water Source  
(MPRV, Tank, Etc.):**

## Test Results

**Nozzle Coefficient:** 0.9

**Measured Flow Rate:** 530 GPM

**Static Pressure:** 95 PSI

**Residual Pressure:** 28 PSI

**Calculated Flow at 20 PSI:** 563.29 GPM

**Comments:**
